
3C05: Unified Software Development Process

Unit 5: Unified Software Development Process

Objectives:

- Introduce the main concepts of iterative and incremental development
- Discuss the main USDP phases

USDP

- USDP is an industry standard software development process
 - Free!
 - The generic process for the UML
- USDP is:
 - Use-case and risk driven
 - Architecture centric
 - Iterative and incremental
- For reference: Ivar Jacobson, Grady Booch, James Rumbaugh: The Unified Software Development Process. Addison Wesley. 1999


USDP for your project...

- USDP is a generic software engineering process. It has to be customised (instantiated) for your project:
 - In-house standards
 - Document templates
 - Tools
 - Databases
 - Lifecycle modifications
- Rational Unified Process is an instantiation of USDP. RUP is a product marketed and owned by Rational Corporation
- RUP also has to be instantiated for your project!


Iterations

- Iterations are the key to the USDP
- Each iteration is like a mini-project including:
 - Planning
 - Analysis and design
 - Integration and test
 - An internal or external release
 - The result of an iteration is an increment
- We arrive at a final product release through a sequence of iterations
- Iterations contain workflows
- Iterations are organised into phases

Iteration Workflows

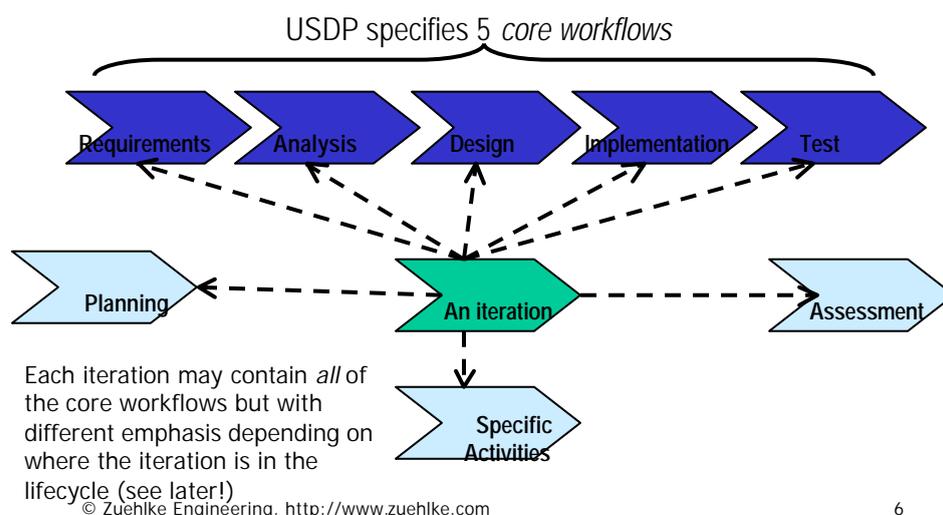

Iterations may overlap

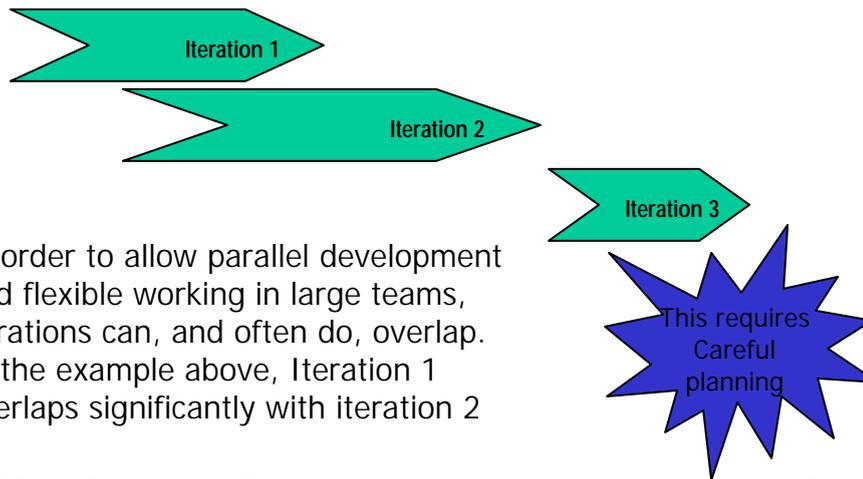

© Zuehlke Engineering, <http://www.zuehlke.com>

7

Increments

- Each iteration generates internal (or external) releases of various artefacts which together constitute a baseline
- A baseline is a set of reviewed and approved artefacts that:
 - Provides an agreed basis for further review and development
 - Can be changed only through a formal procedure such as configuration and change management
- An increment is the difference between the release of one iteration and the release of the next
 - The result of an iteration is an increment


© Zuehlke Engineering, <http://www.zuehlke.com>

8

USDP Lifecycle


- The USDP lifecycle is divided into a sequence of phases
- Each phase may include many iterations
 - The exact number of iterations per phase depends on the size of the project!
 - One iteration per phase for small projects
- Each phase concludes with a major milestone

USDP Phases

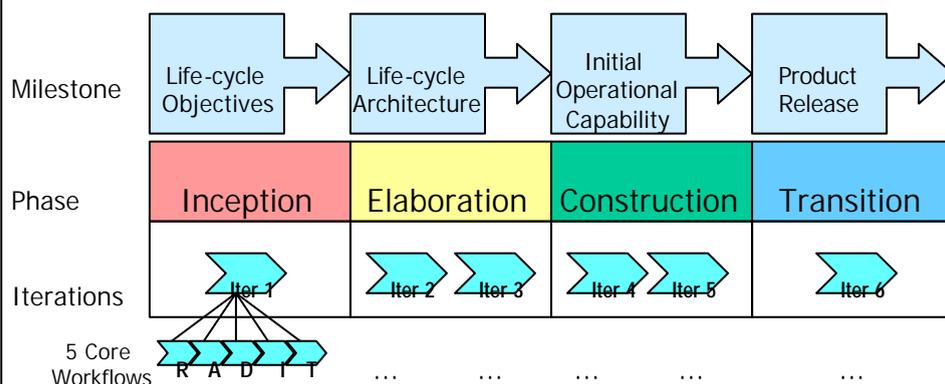

The exact number of iterations per Phase depends on the size of the project!
 We have assumed a that this particular project lasts 18 months.


Phases and Workflows

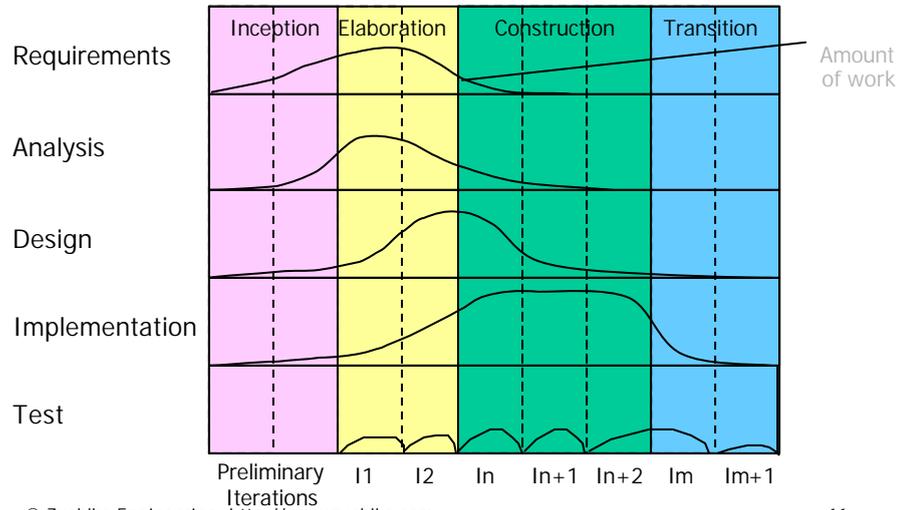

© Zuehlke Engineering, <http://www.zuehlke.com>

11

Time for a typical project

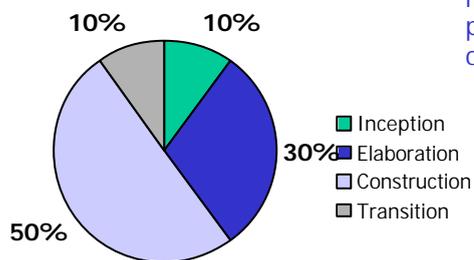


•If we consider a project of "typical" difficulty, then this is how the total time for the project is likely to be distributed over the phases

© Zuehlke Engineering, <http://www.zuehlke.com>

12

Time for a difficult project

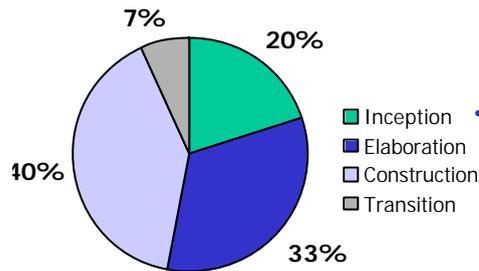


- If we consider a project of greater than normal difficulty, then this is how the total time for the project is likely to be distributed over the phases
- Note that for more difficult projects more time is spent in the early phases

© Zuehlke Engineering, <http://www.zuehlke.com>

13

Resource for a typical project

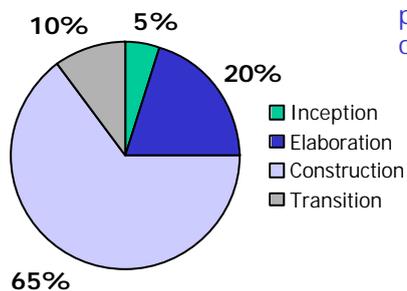


- If we consider a project of "typical" difficulty, then this is how the total resource for the project is likely to be utilised over the phases

© Zuehlke Engineering, <http://www.zuehlke.com>

14

Resource for a difficult project

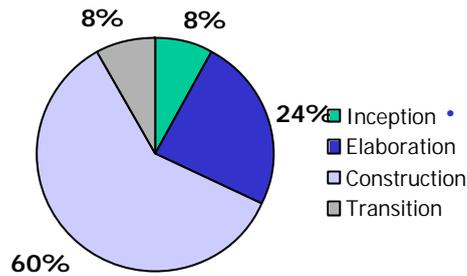


- If we consider a project of greater than normal difficulty, then this is how the total resource for the project is likely to be distributed over the phases
- Note that for more difficult projects more resource is used in the early phases

Phases

- For each phase we will consider:
 - The goal for the phase
 - The focus in terms of the core workflows
 - The milestone at the end of the phase



Inception




Inception - Goals



- Establish feasibility of the project
- Create a business case
- Capture key requirements
- Scope the system
- Identify critical risks
- Create proof of concept prototype

Phases and Workflows

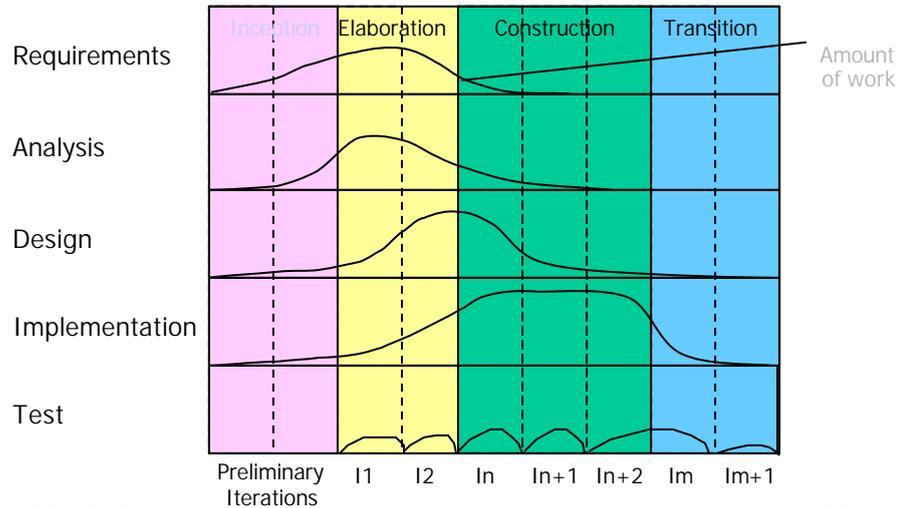

© Zuehlke Engineering, <http://www.zuehlke.com>

19

Inception - Focus



- Requirements – establish business case, scope and core requirements
- Analysis – establish feasibility
- Design – design proof of concept or technical prototypes
- Implementation – build the proof of concept prototype
- Test – not generally applicable

N.B. The blue bars indicate approximately the relative amount of resource needed

© Zuehlke Engineering, <http://www.zuehlke.com>


20

Life Cycle Objectives



- Conditions of satisfaction:
 - System scope has been defined
 - Key requirements for the system have been captured. These have been defined and agreed with the stakeholders
 - An architectural vision exists. This is just a sketch at this stage
 - A Risk Assessment
 - A Business Case
 - Project feasibility is confirmed
 - The stakeholders agree on the objectives of the project

Elaboration




Elaboration - Goals



- Create an executable architectural baseline
- Refine Risk Assessment
- Define quality attributes (defect rates etc.)
- Capture use-cases to 80% of the functional requirements
- Create a detailed plan for the construction phase
- Formulate a bid which includes resources, time, equipment, staff and cost

Phases and Workflows

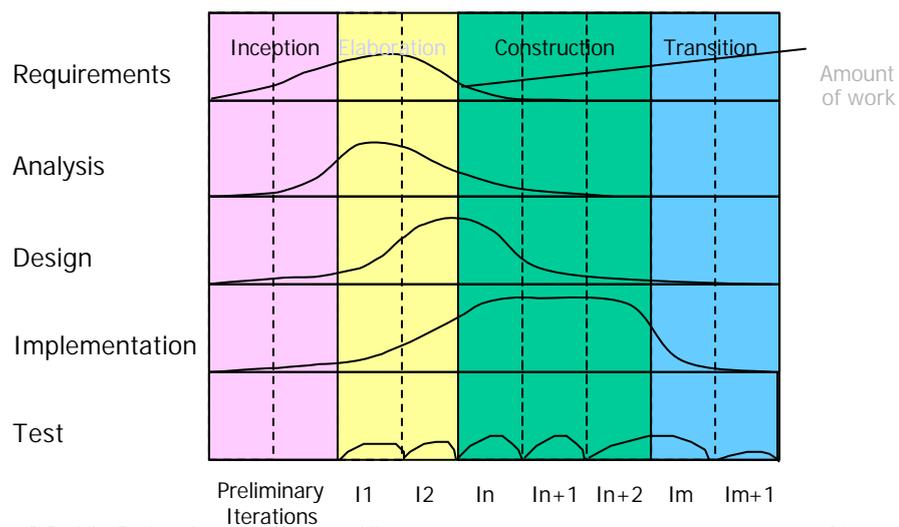

How many use-cases?

- Our goal is to find sufficient use-cases to allow us to build a system
- Aim to *identify* about 80% of the use-cases based on a consideration of functional requirements
 - The other 20% will come out in later phases if important
- Aim to *model in detail* only about 40% to 80% of the set of identified use-cases
- For each use-case modelled in detail, only a small fraction of the possible scenarios may need to be modelled

Model *just enough* use-cases to capture the information you need!

Elaboration - Focus




- Requirements – refine system scope and requirements
- Analysis – establish what to build
- Design – create a stable architecture
- Implementation – build the architectural baseline
- Test – test the architectural baseline

Life Cycle Architecture



- Conditions of satisfaction:
 - A resilient, robust executable architectural baseline has been created
 - The Risk Assessment has been updated
 - A project plan has been created to enable a realistic bid to be formulated
 - The business case has been verified against the plan
 - The stakeholders agree to continue

Construction




Construction - Goals



- Completing use-case identification, description and realisation
- Finish analysis, design, implementation and test
- Maintain the integrity of the system architecture
- Revise the Risk Assessment

Phases and Workflows

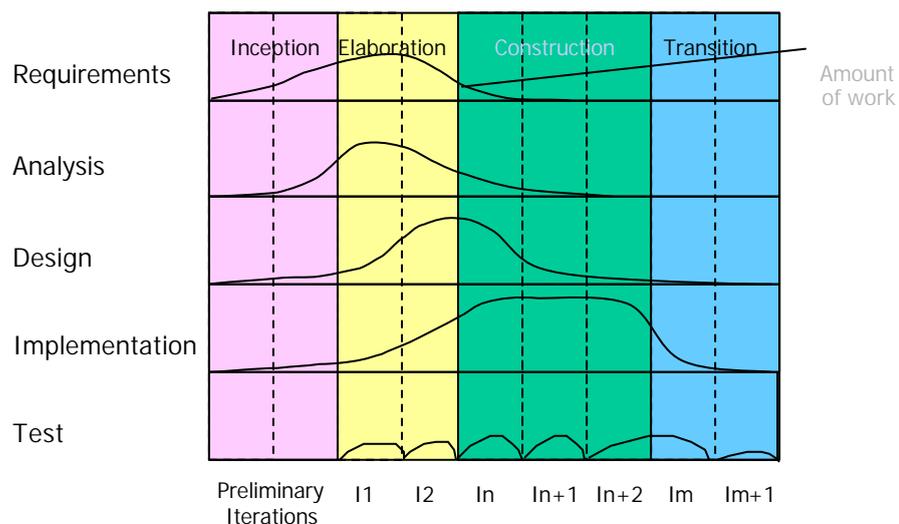


Construction - Focus



- ▮ Requirements – uncover any requirements that had been missed
- ▮ Analysis – finish the analysis model
- ▮ Design – finish the design model
- ▮ Implementation – build the Initial Operational Capability
- ▮ Test – test the Initial Operational Capability

Plan for two lines of work...

About 10 to 20% of the resources will not contribute directly to the next release!

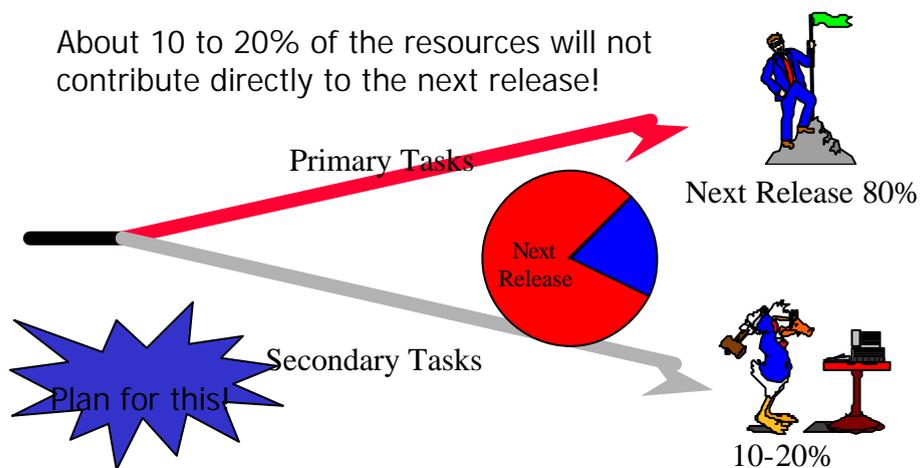

Primary and secondary tasks


- Primary tasks:
 - Everything that contributes directly to the next increment
- Secondary tasks:
 - Everything else!
 - Attack risks with behavioural prototypes
 - Solve critical problems with taskforces (tiger teams)
 - Research into problem and solution domains
 - Bug tracking and reporting

Initial Operational Capability



- Conditions of satisfaction:
 - The product is ready for beta testing in the user environment

Transition




Transition - Goals



- Correct defects
- Prepare the users site for the new software
- Tailor the software to operate at the users site
- Modify software if unforeseen problems arise
- Create user manuals and other documentation
- Provide customer consultancy
- Conduct post project review

Phases and Workflows

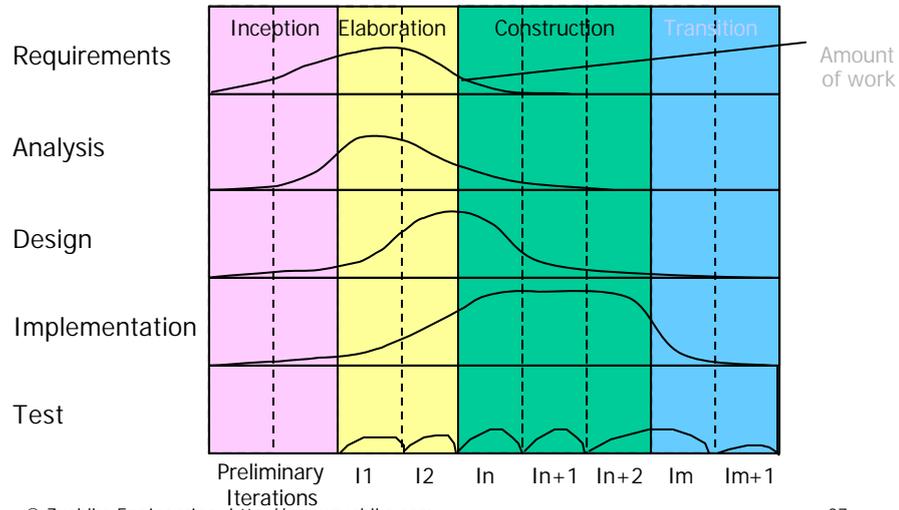

Transition - Focus



- Requirements – not applicable
- Analysis – not applicable
- • Design – modify the design if problems emerge in beta testing
- • Implementation – tailor the software for the users site and correct problems uncovered in beta testing
- • Test – beta testing and acceptance testing at the users site

Product Release



- Conditions of satisfaction:
 - Beta testing, acceptance testing and defect repair are finished
 - The product is released into the user community

Key Points

- USDP is the iterative and incremental software engineering process for the UML
- USDP has four phases:
 - Inception
 - Elaboration
 - Construction
 - Transition
- Each phase may have one or more iterations
- Each iteration has five iteration workflows
 - Requirements, Analysis, Design, Implementation, Test
